3rd TRACK CONSTRUCTORS

Picone | Dragados USA | CCA Civil | Halmar

Night Shift

Day Shift

LIRR Contract # 6240	2/25/2019
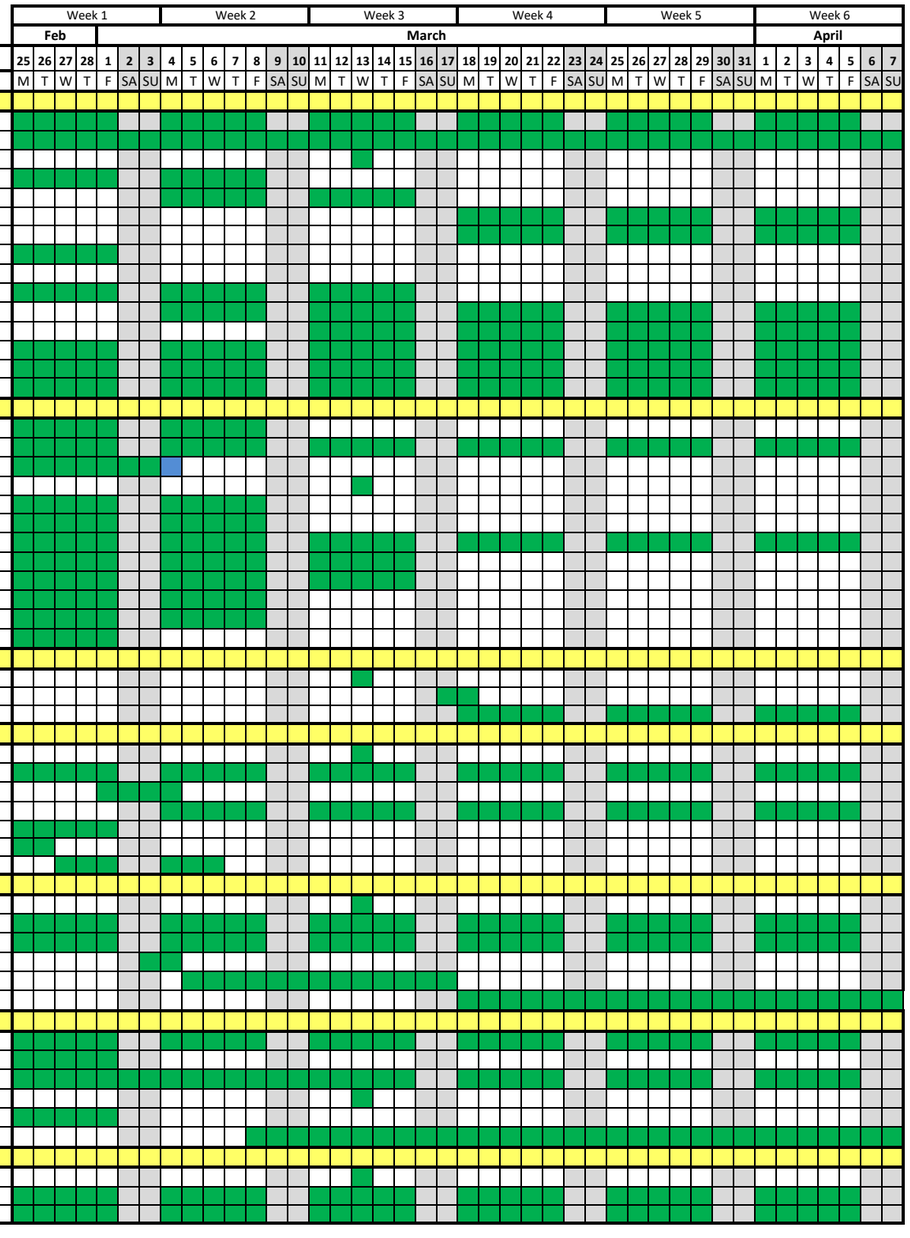
Village	Type of work	Sub contractor	Street Location
FLORAL PARK			
Floral Park	G-13 Substation- deliveries and site work	3TC	Plainfiled ave
Floral Park	Carnation Property- use yard for storage	3TC	Lilly Street, Carnation
Floral Park	Rodent Control along LIRR Fence		Plainfield ave-Linden Ave
Floral Park	Core drill east abutment for future tie backs	3TC	South Tyson Viaduct-East Side
Floral Park	Install tiebacks at East abutment	3TC	South Tyson Viaduct-East Side
Floral Park	Excavate East abutment	3TC	South Tyson Viaduct-East Side
Floral Park	Demo East abutment	3TC	South Tyson Viaduct-East Side
Floral Park	Verizon cable relocations	3TC	Plainfield up Covert Ave
Floral Park	Test pit area by Linden Ave underpassage-Soouth Side	3TC	Linden Ave
Floral Park	Drill Soldier piles for SOE South Side	3TC	Linden Ave
Floral Park	Demo Underpass	3TC	Linden Ave
Floral Park	Install mini piles	3TC	Linden Ave
Floral Park	Temp utility pole relocation along the ROW-North and South Side	3TC-Verizon	Plainfeld to New Hyde Park Rd
Floral Park	Excavate and grade access road	3TC	Plainfeld/Terrace Ave
Floral Park	Install SOE-Support of Excavation	3TC	Plainfeld/Terrace Ave
NEW HYDE PARK			
New Hyde Park	Temporary fire house istallation-froundations	3TC	S12St
New Hyde Park	Street Utitlity work installation	3TC	Covert Ave, S2nd, S3rd
New Hyde Park	Relocate transmission service at Covert Ave	EJ Elec	Covert Ave
New Hyde Park	Rodent Control along LIRR Fence		Covert Ave to S18th St
New Hyde Park	Widen sidewalk and ramp at South Covert Ave		South Covert Ave
New Hyde Park	Widen sidewalk and ramp at North Covert Ave		North Covert Ave
New Hyde Park	Early work-South stage 1A install soldier piles 16pcs		South Covert Ave
New Hyde Park	New Hyde Park Rd water main installation	3TC	New Hyde Park Rd
New Hyde Park	New Hyde Park Rd sanitary line installation	3TC	New Hyde Park Rd
New Hyde Park	Gas Main Reroute	National Grid	New Hyde Park Rd
New Hyde Park	Gas Main installation under tracks	National Grid	New Hyde Park Rd
New Hyde Park	Transmission service relocation at New Hyde Park Rd	National Grid	New Hyde Park Rd
GARDEN CITY/GARDEN CITY PARK			
Garden City	Rodent Control along LIRR Fence		
Garden City	Merillon Station partial shutdown of the west end both south and north side 12:01AM Sunday into Monday	3TC	Merillon Station
Garden City	Preliminary demoliton of Merillon Station	3TC	Merillon Station
MINEOLA			
Mineola	Rodent Control along LIRR Fence		Herricks Road to Glen Cove Road
Mineola	SOE installation, Excavation	Oliviera,UFS	Harrison Ave
Mineola	Electrical relocations	EJ Elec	Harrison Ave
Mineola	Cast in place footings and grade beams	Oliviera	Harrison Ave
Mineola	Hand test pits along the ROW	3TC	Mineola road to Westbury station
Mineola	Directional utility drilling	Verizon	Roslyn Rd
Mineola	Directional utility drilling	Verizon	Main St
NORTH HEMPSTEAD CARLE PLACE			
Carle Place	Rodent Control along LIRR Fence		Glen Cove Road to Carle Road
Carle Place	Install SOE-Support of Excavation	3TC	Cherry Lane-Atlantic Ave
Carle Place	Install SOE-Support of Excavation	3TC	Carle Place Station South side/North Side
Carle Place	North West platform taken out of service 12:01AM Sunday into Monday	3TC	Carle Place Station North Side
Carle Place	Demoltion of exisitng palform	3TC	Carle Place Station North Side
Carle Place	Reconstruciton of new platform	3TC	Carle Place Station North Side
NORTH HEMPSTEAD NEW CASSEL			
New Cassel	Utilize LIRR G-19	3TC	Broadway
New Cassel	Street Utitlity work-Sanitary North East run	3TC	Urban Ave
New Cassel	Preliminary pile installaiton on north/south side of Urban Ave-MPT	3TC	Urban Ave
New Cassel	Rodent Control along LIRR Fence		School St to Wantagh State Parkway
New Cassel	Utility pole installation along the ROW	EJ Elec	School to Urban Ave
New Cassel	Urban Ave shutdown	3TC	Urban Ave
WESTBURY			
Westbury	Rodent Control along LIRR Fence		Carle Road to School st
Westbury	Excavate to subgrade south side along the LIRR ROW		School St to Urban Ave
Westbury	Drill Soldier piles along the ROW south side		School St to Urban Ave
